

*2/1/72* *B-1*

POR-6741  
(WT-6741)

**MIDDLE NORTH SERIES  
DIAL PACK EVENT**

**PROJECT OFFICERS REPORT**

**PROJECT LN-318**

**TEST OF PRECAST CONCRETE  
UNDERGROUND STRUCTURE (U)**

**HEADQUARTERS  
DEFENSE NUCLEAR AGENCY  
WASHINGTON, D.C. 20305**

**20000908 130**

Issuance date: 24 November 1972

**APPROVED FOR PUBLIC RELEASE  
DISTRIBUTION UNLIMITED**

**DEIC QUALITY INSPECTED 4**

**Reproduced From  
Best Available Copy**

**9240**

Destroy this report when it is no longer needed.  
Do not return to sender.

Retention of this document by DOD Contractors  
or Consultants is authorized in accordance with  
Paragraph 2, Industrial Security Letter 71L-3,  
dated 17 May 1971.

POR-6741  
(WT-6741)

MIDDLE NORTH SERIES

DIAL PACK EVENT

PROJECT OFFICERS REPORT—PROJECT LN-318

TEST OF PRECAST CONCRETE UNDERGROUND STRUCTURE (U)

HEADQUARTERS  
DEFENSE NUCLEAR AGENCY  
WASHINGTON, D. C. 20305

R. W. Mayo, Project Officer  
Bell Laboratories  
Whippany Road  
Whippany, New Jersey 07981

APPROVED FOR PUBLIC RELEASE  
DISTRIBUTION UNLIMITED

THIS PAGE IS INTENTIONALLY LEFT BLANK.

## ABSTRACT

DIAL PACK Event of the MIDDLE NORTH Series, Bell Laboratories Project LN-318, involved the evaluation of the blast-induced response of the SA Manhole. The SA Manhole was a full-size, segmented, precast-concrete hardened structure, to be used by the Long Lines Department of American Telephone and Telegraph Company, to house electronic repeater equipment. Testing was designed to determine the extent of cracking, equipment environments, and overall structural response.

THIS PAGE IS INTENTIONALLY LEFT BLANK.

## TABLE OF CONTENTS

	<u>Page</u>
Abstract - - - - -	iii
Introduction - - - - -	1
Procedure - - - - -	2
Results - - - - -	25
Conclusions - - - - -	32

## LIST OF ILLUSTRATIONS

<u>Figure</u>		<u>Page</u>
1	Load impulse from impingement to natural vibration period -----	3
2	Model of the SA Manhole -----	4
3	Elevation view of the SA Manhole -----	5
4	Assembly of Manhole (page 1 of 10) -----	6
5	Assembly of Manhole (page 2 of 10) -----	7
6	Assembly of Manhole (page 3 of 10) -----	8
7	Assembly of Manhole (page 4 of 10) -----	9
8	Assembly of Manhole (page 5 of 10) -----	10
9	Assembly of Manhole (page 6 of 10) -----	11
10	Assembly of Manhole (page 7 of 10) -----	12
11	Assembly of Manhole (page 8 of 10) -----	13
12	Assembly of Manhole (page 9 of 10) -----	14
13	Assembly of Manhole (page 10 of 10) -----	15
14	Blast hatch used on SA Manhole -----	16
15	Test installation-----	18
16	Elevation view of the conduit installation -----	20
17	Installation of the PVC conduit -----	21
18	Instrumentation -----	23
19	Postshot view of the blast hatch -----	26
20	Main conduit vertical axial deformations -----	30



## LIST OF TABLES

<u>Table</u>		<u>Page</u>
1	Recorded measurements of rebound forces - - - - -	27
2	Diagonal measurements of structure interior - - - - -	29
3	Recorded peak values - - - - -	28

THIS PAGE IS INTENTIONALLY LEFT BLANK.

## INTRODUCTION

The primary objective of the DIAL PACK Event was to evaluate the blast-induced response of a full-size, segmented, precast-concrete hardened structure. Such a structure will be used by the Long Lines Department of American Telephone and Telegraph Company to house electronic repeater equipment on hardened L4 and L5 coaxial cable routes. In addition, this type of construction is being considered for use in larger underground buildings.

The existing L4 and planned L5 carrier systems are nationwide, high-capacity communication systems providing telephone circuits for civilian and military needs. These coaxial cable systems are hardened to survive the collateral effects of nuclear weapon attack. The communication system itself is not considered to be a target but is hardened to survive the effects of a nuclear weapon attack on nearby targets. The cable systems are routed to avoid targets by margins sufficient to preclude blast effects exceeding the design environment of the system.

The auxiliary repeater stations, or manholes, are all designed to survive 50-psi blast effects. The coaxial cable has a blast resistance exceeding 100 psi, even when buried at a shallow depth. These cables are buried at a minimum depth of 4 feet to reduce the likelihood of accidental dig-ups.

## PROCEDURE

The structure tested in the DIAL PACK Event, the SA Manhole, was designed to survive a 50-psi blast loading due to the detonation of a megaton nuclear weapon with only minor plastic deformation.

A consideration of the impulse differences between the DIAL PACK Event and a megaton nuclear blast indicated the placement of the structure at a range corresponding to 60-psi overpressure in DIAL PACK Event (see figure 1). The test was designed to determine the extent of cracking, blast-induced deflections and relative motions, equipment environments, and overall structural response.

Figure 2 shows a model of the SA Manhole. The basic structure was made up of 12 precast concrete slabs, each 8-1/2 inches thick and roughly 9- by 13-feet in area. The interior dimensions of the structure were 12- by 24- by 8-feet. A structural steel frame supported the roof at mid-span, and a concrete collar section with a blast-hatch was mounted in the entry area and permitted a cover of 2 feet of earth over the roof of the structure. The blast-hatch, 2- by 6-feet in area, was made of cast aluminum in two parts; the sections folded to completely open the hatch area.

The principal data sought in this experiment were in the following areas:

- (1) load deflection and relative motion of the wall- and roof-slab sections, (2) accelerations on wall- and roof-locations to which equipment might be mounted, (3) shear-strength of the interlocking slab joints, and (4) performance of the new two-piece rolling blast-door, including information on rebound forces.

An elevation view of the installed manhole is shown in figure 3. An earth cover of approximately 2 feet was provided over the roof, sloping back to the original grade with about a 4 on 1 slope.

Figures 4 through 13 show the assembly of the manhole. Shown in figure 14 is the blast hatch used on the SA Manhole. Normally, the hatch was latched in place by means of four bars, activated either by handles from within, or from the outside by means of a special wrench. In the DIAL PACK Event, each hatch-half was bolted with four bolts. One set consisted of instrumented strain bolts which permitted determination of rebound forces.

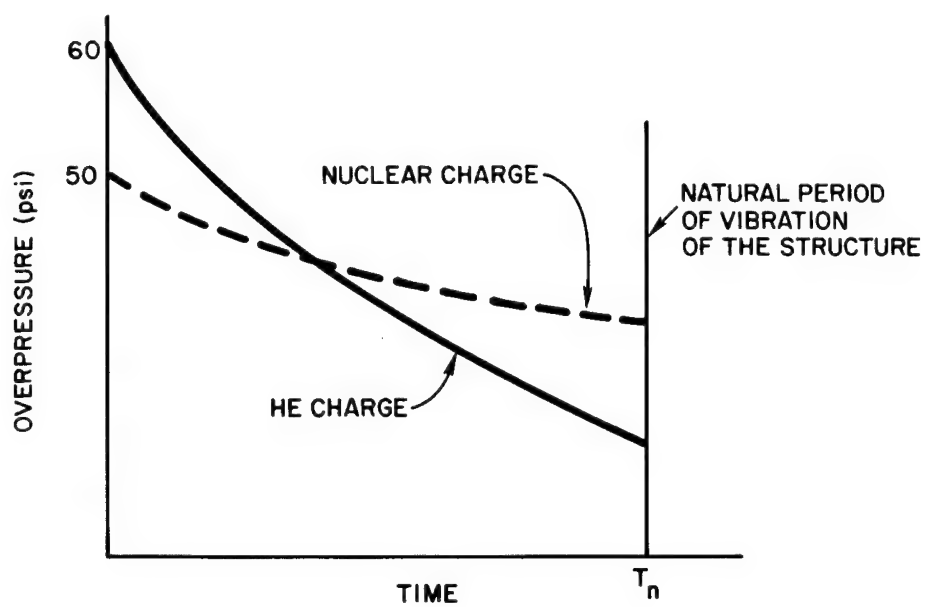


Figure 1. --Load impulse from impingement to natural vibration period.

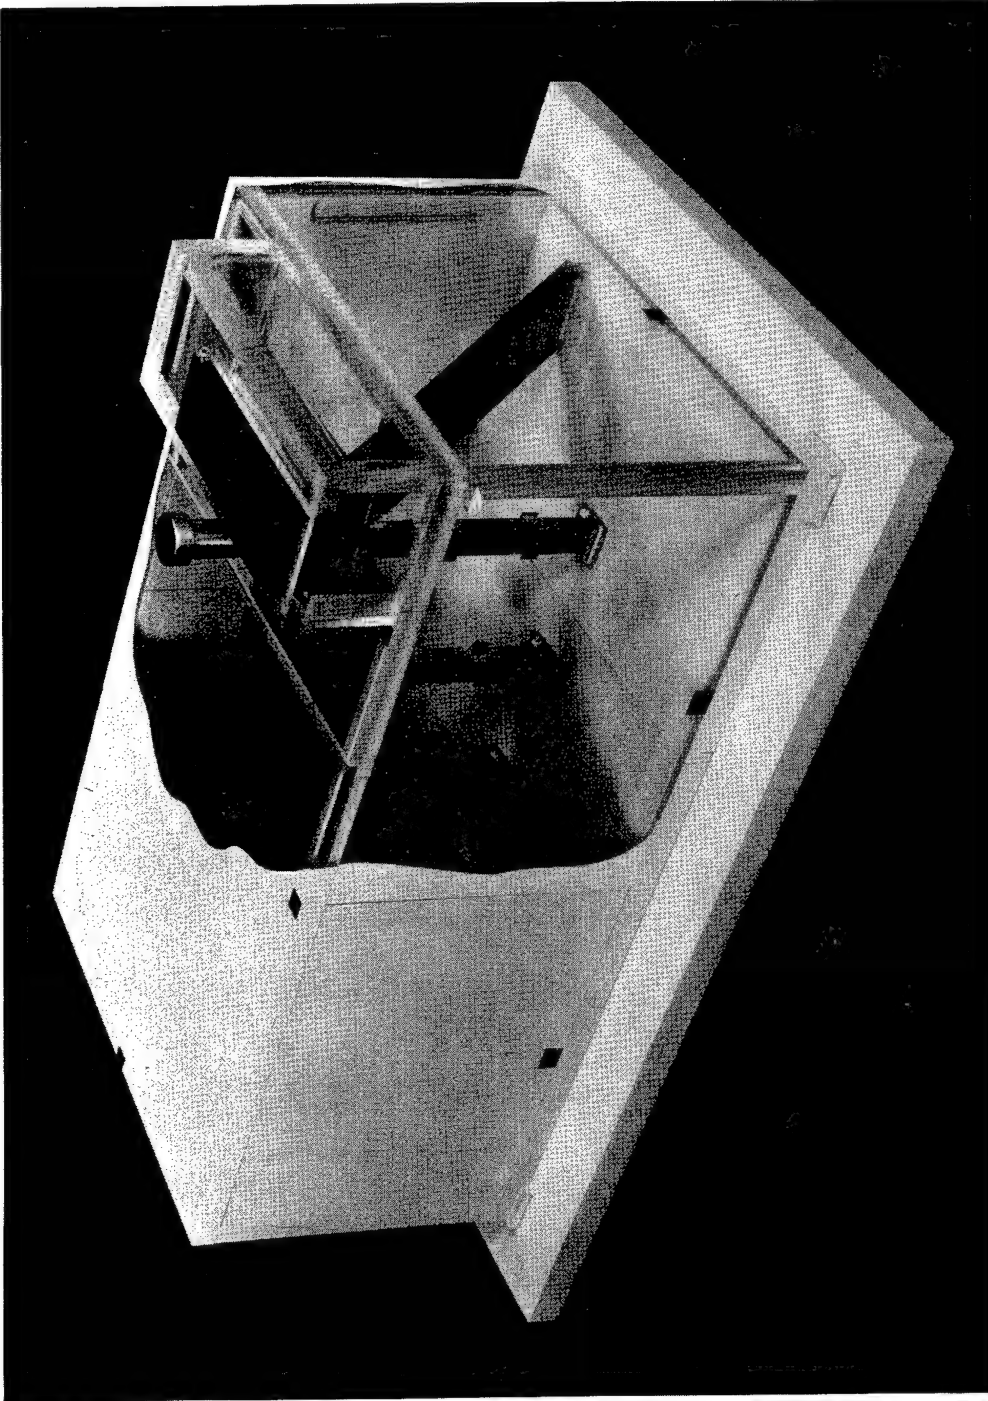


Figure 2. ---Model of the SA Manhole.

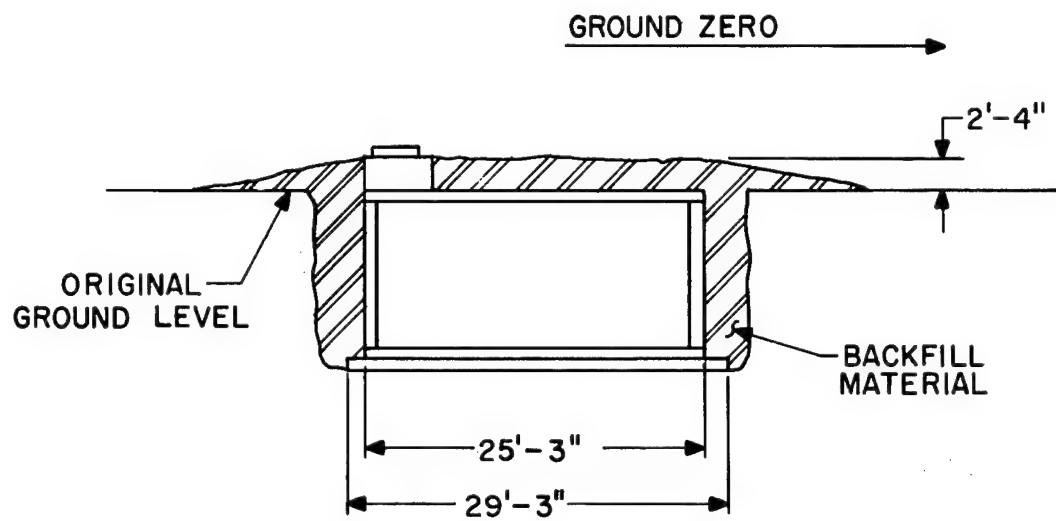


Figure 3. --Elevation view of the SA Manhole.

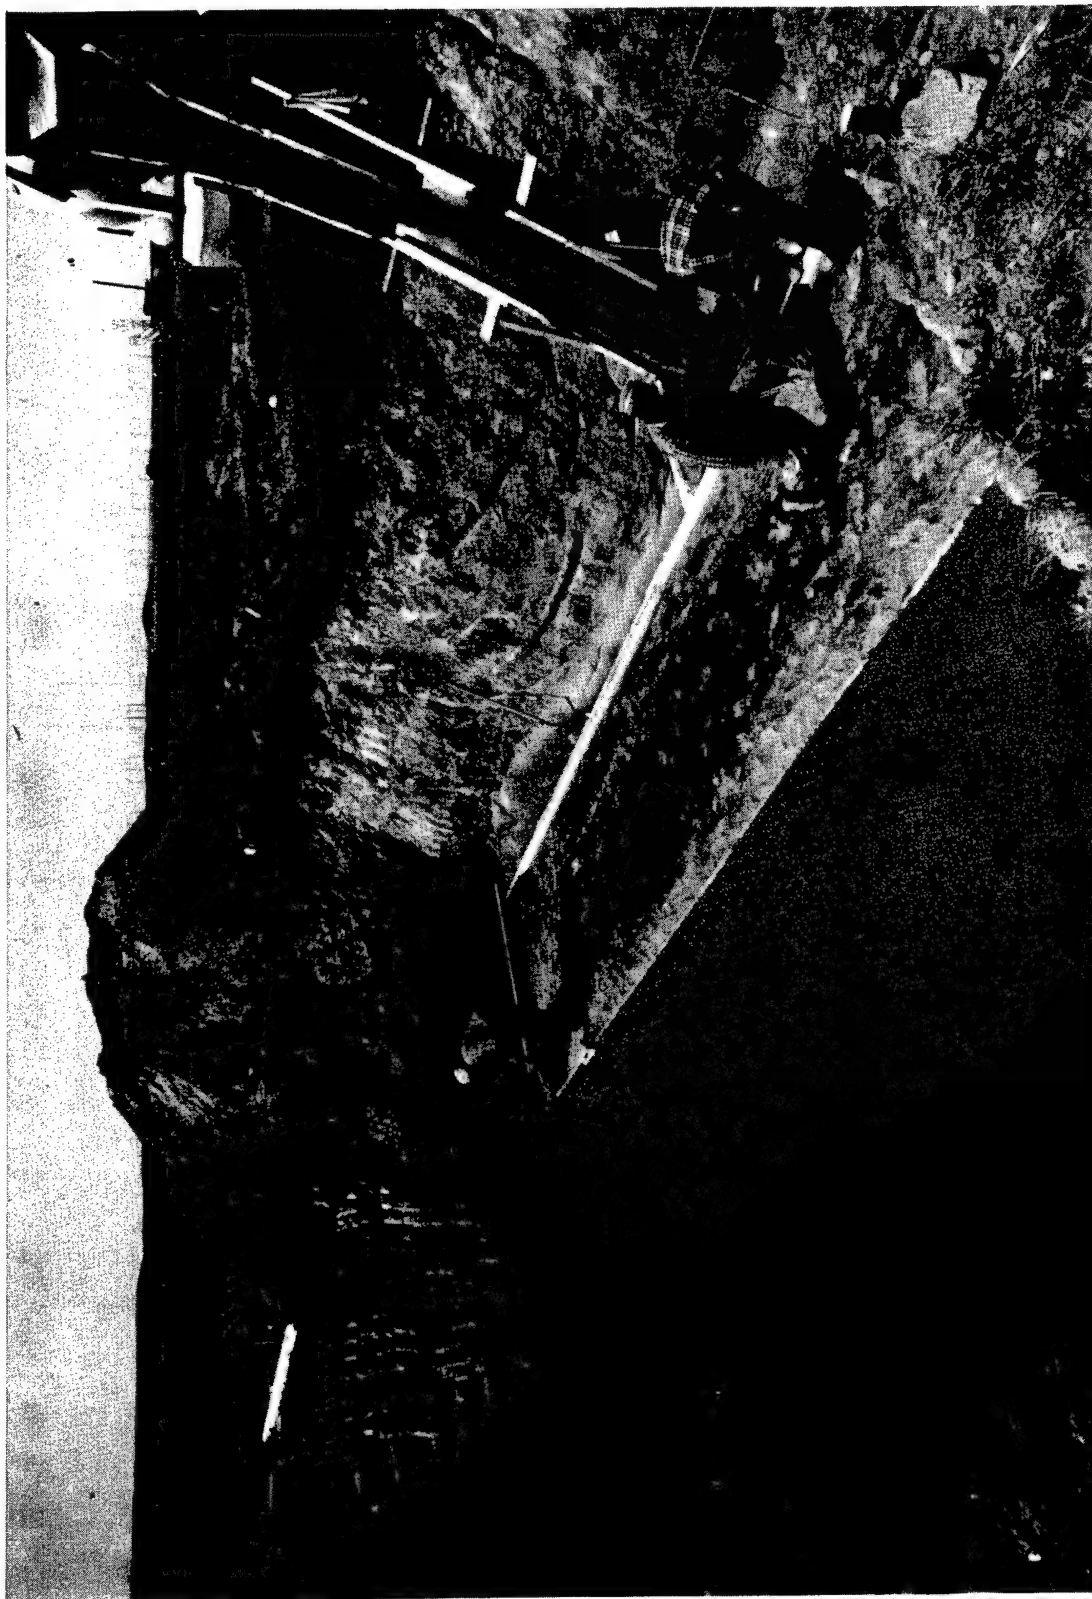


Figure 4. --Assembly of Manhole (page 1 of 10).





Figure 5. ---Assembly of Manhole (page 2 of 10).



Figure 6. ---Assembly of Manhole (page 3 of 10).



Figure 7. --Assembly of Manhole (page 4 of 10).

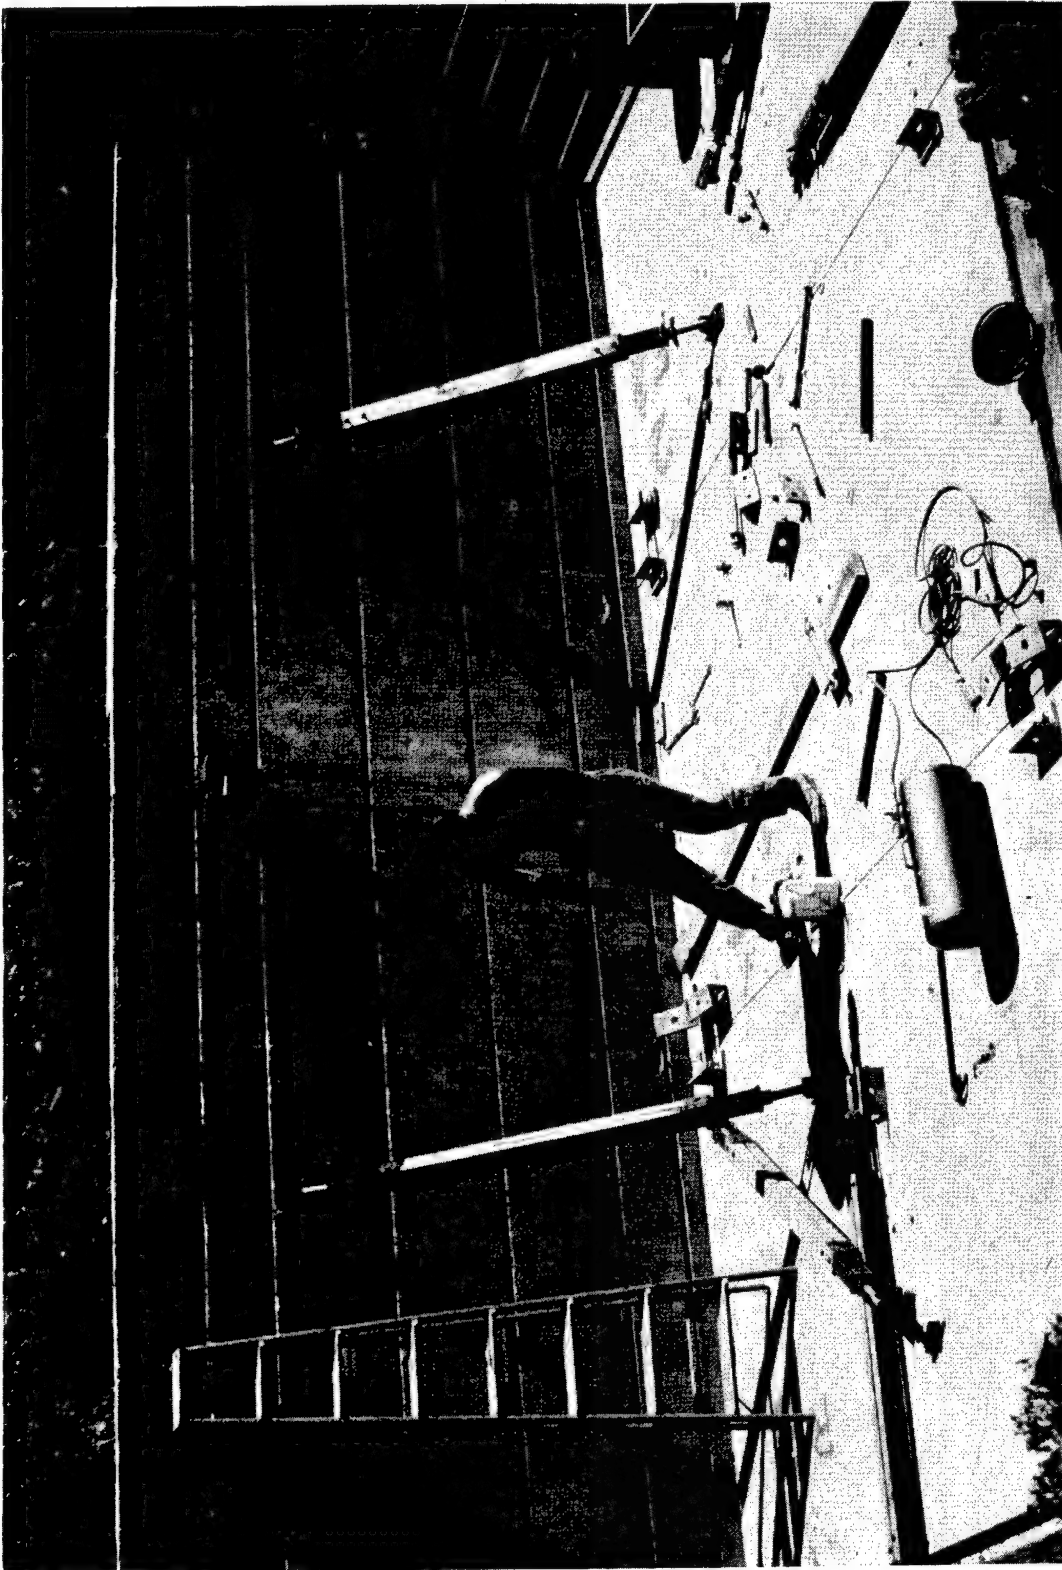


Figure 8. --Assembly of Manhole (page 5 of 10).



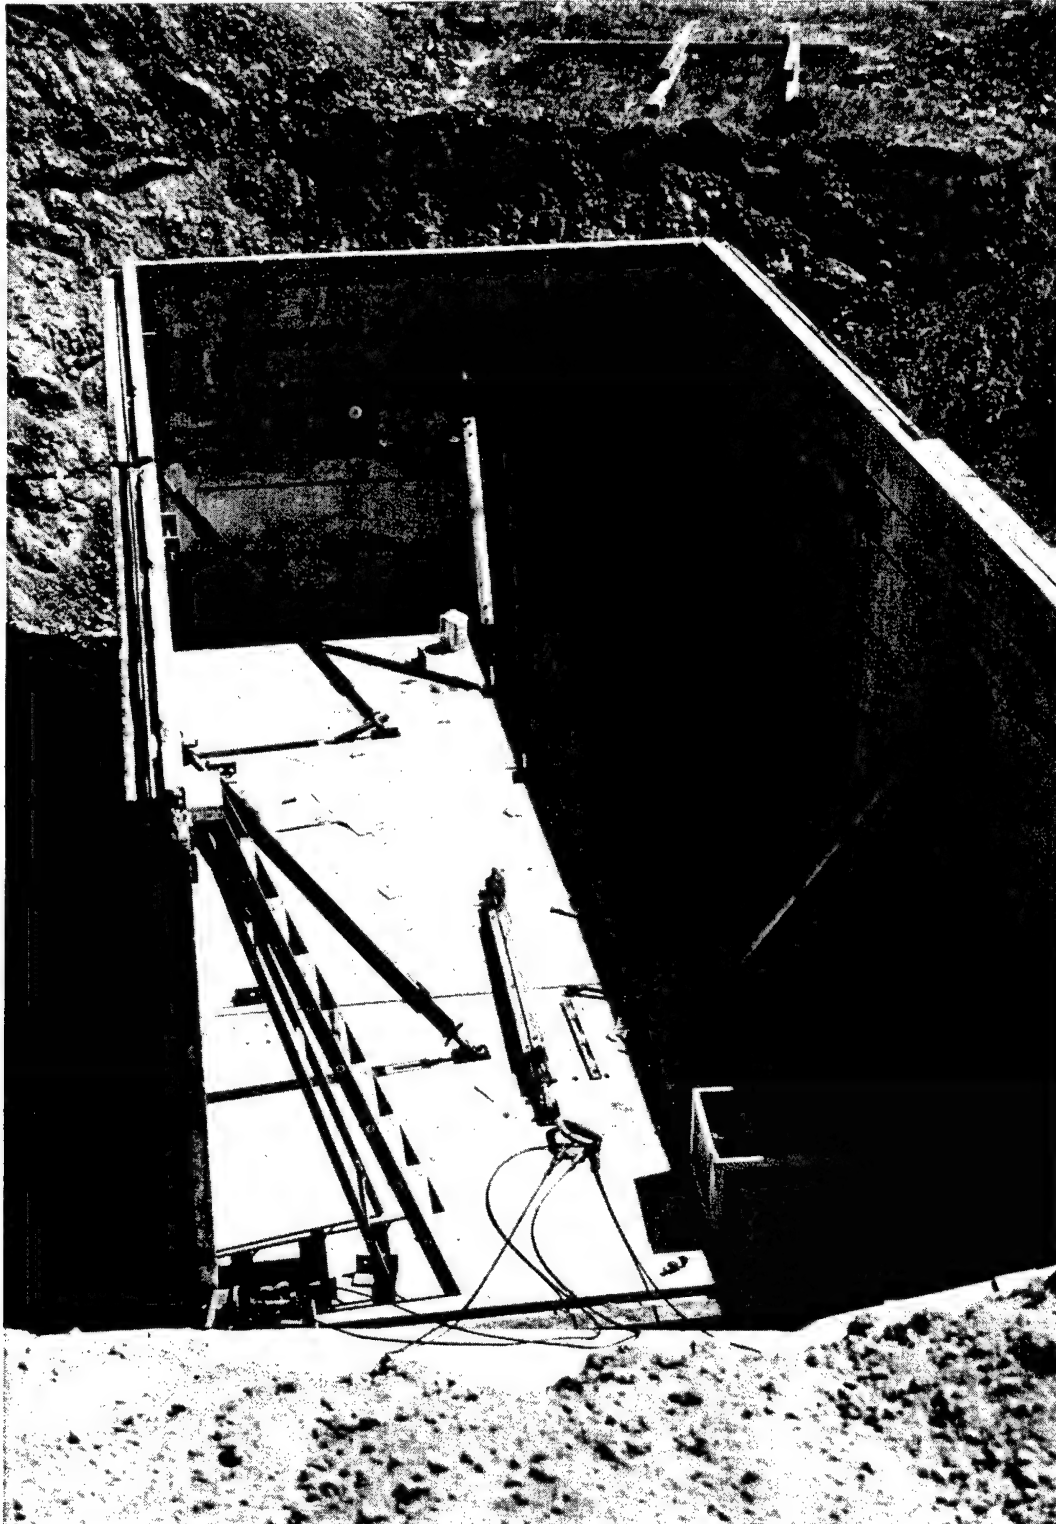


Figure 9. --Assembly of Manhole (page 6 of 10).

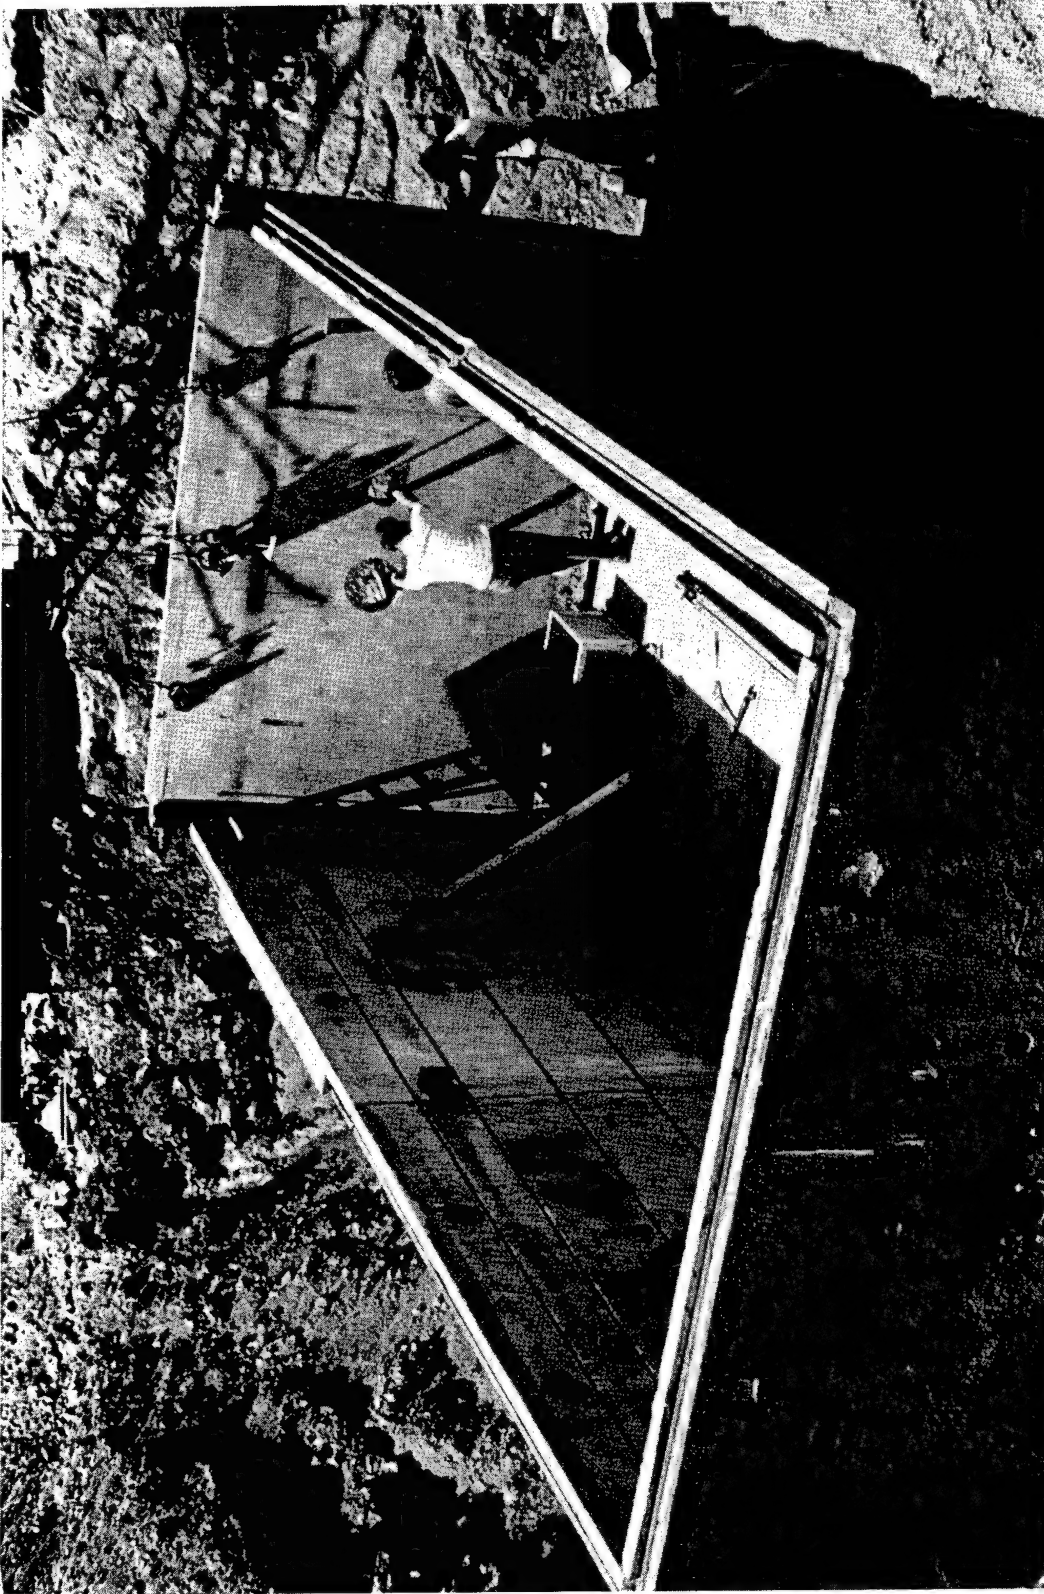


Figure 10. --Assembly of Manhole (page 7 of 10).

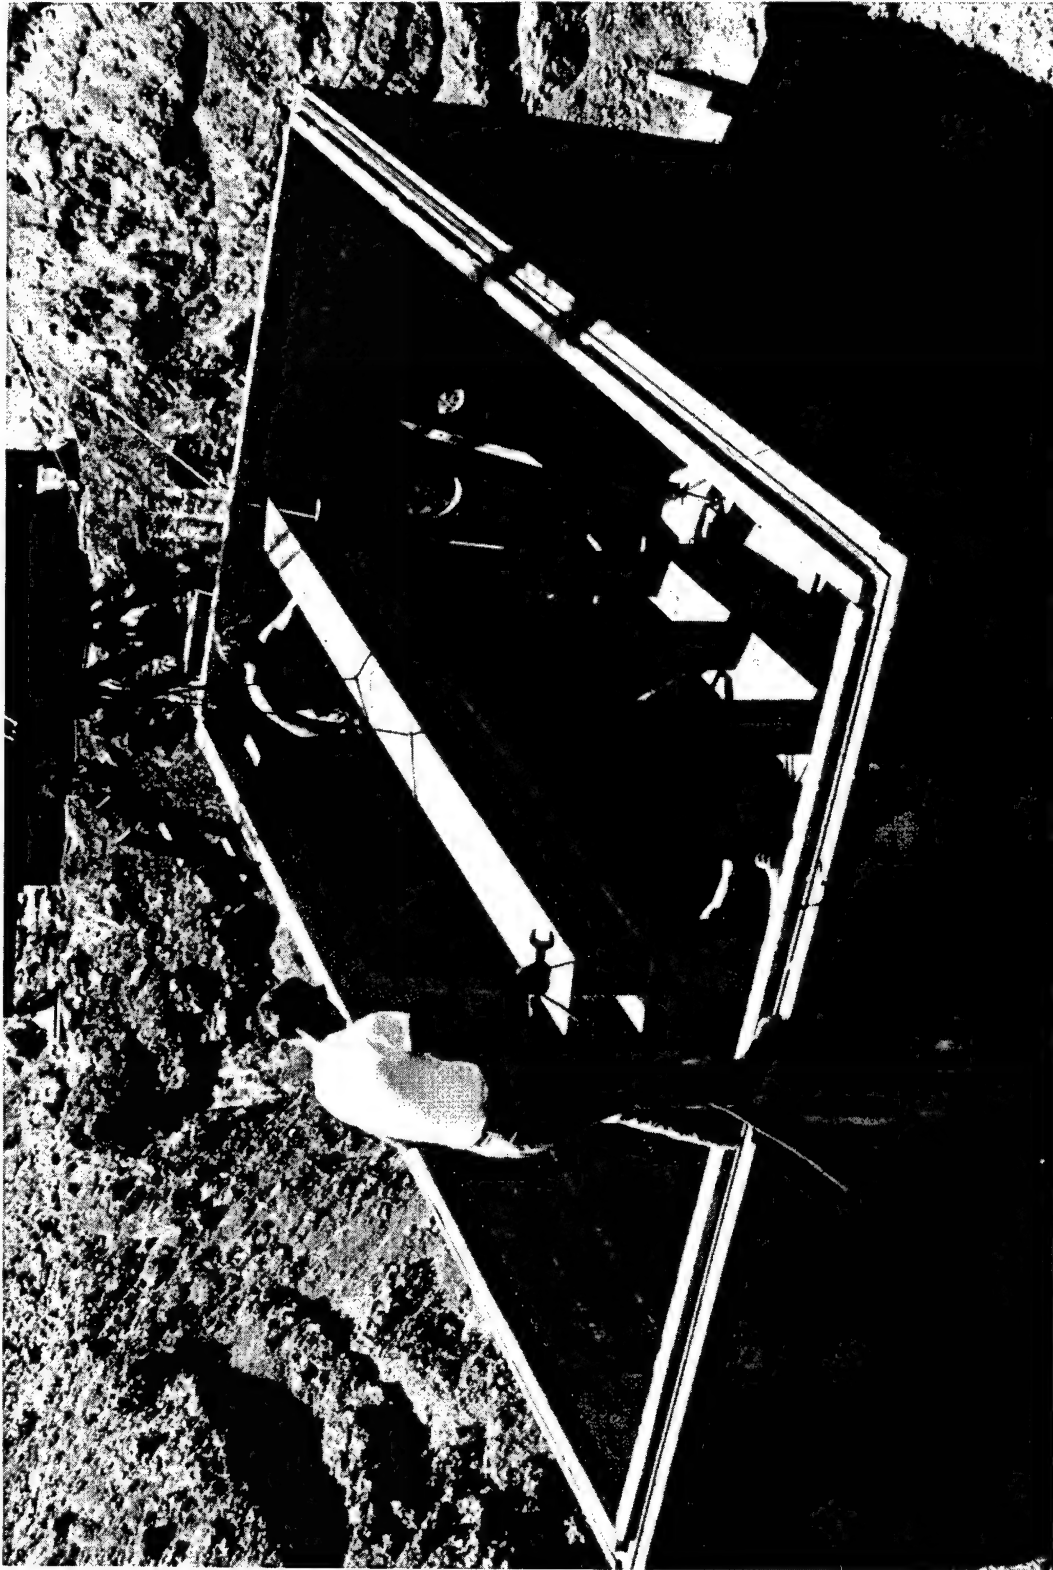


Figure 11. ---Assembly of Manhole (page 8 of 10).

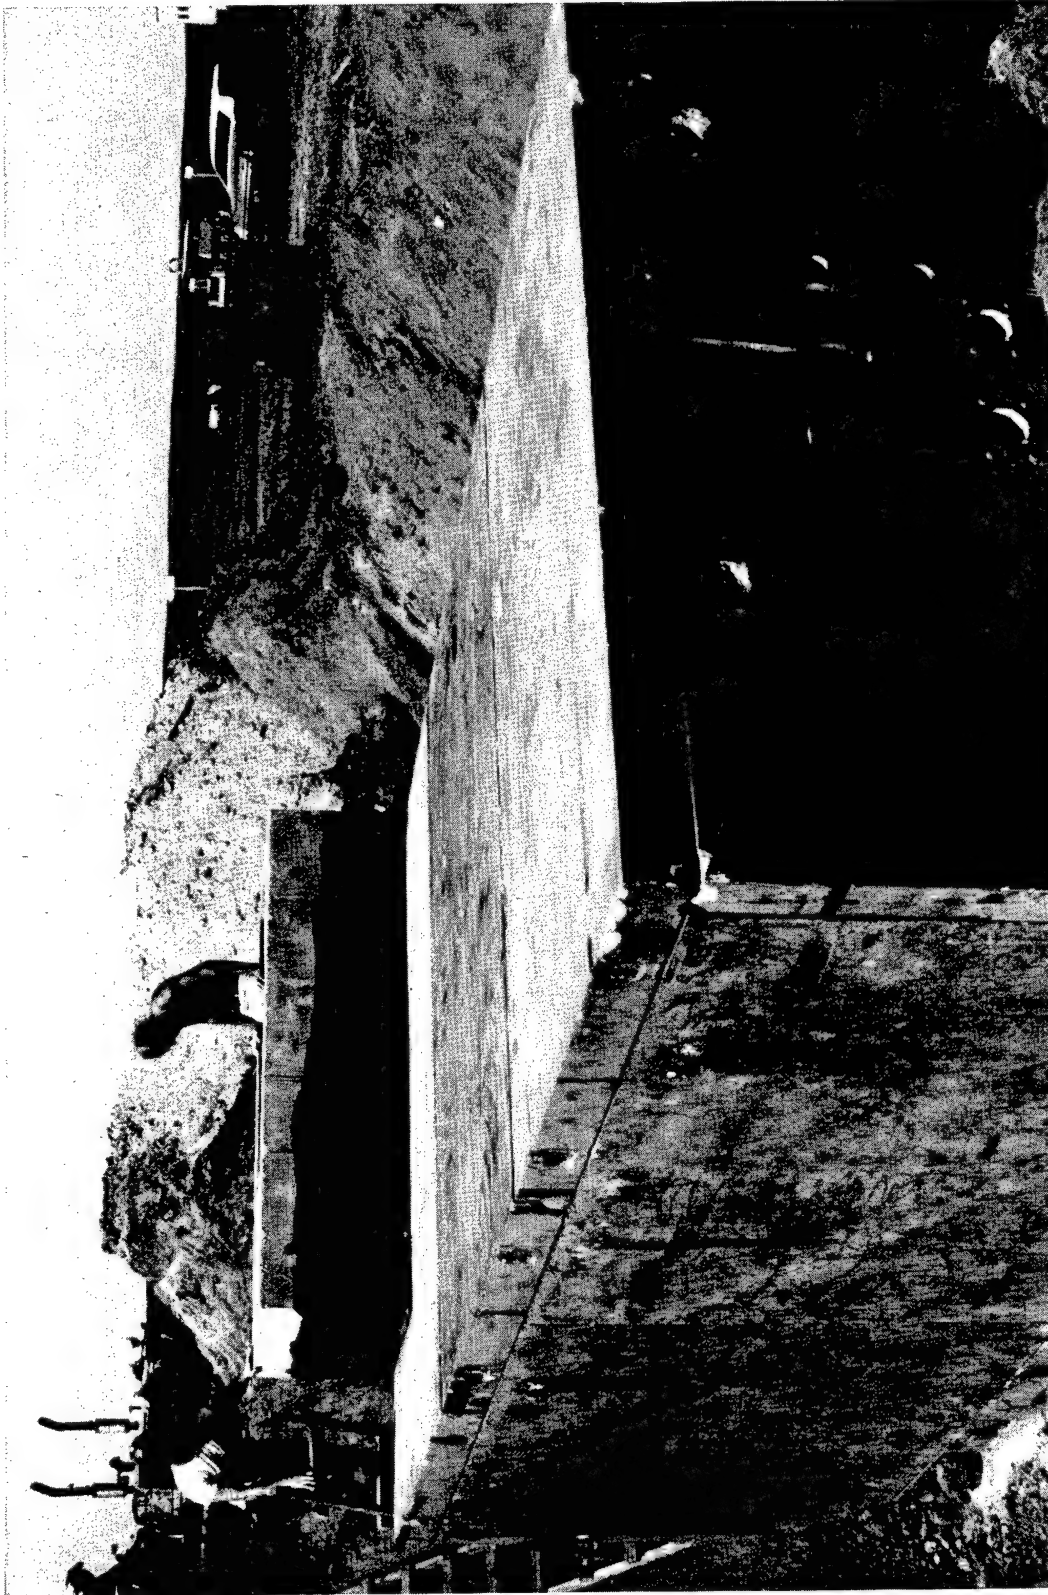


Figure 12. --Assembly of Manhole (page 9 of 10).



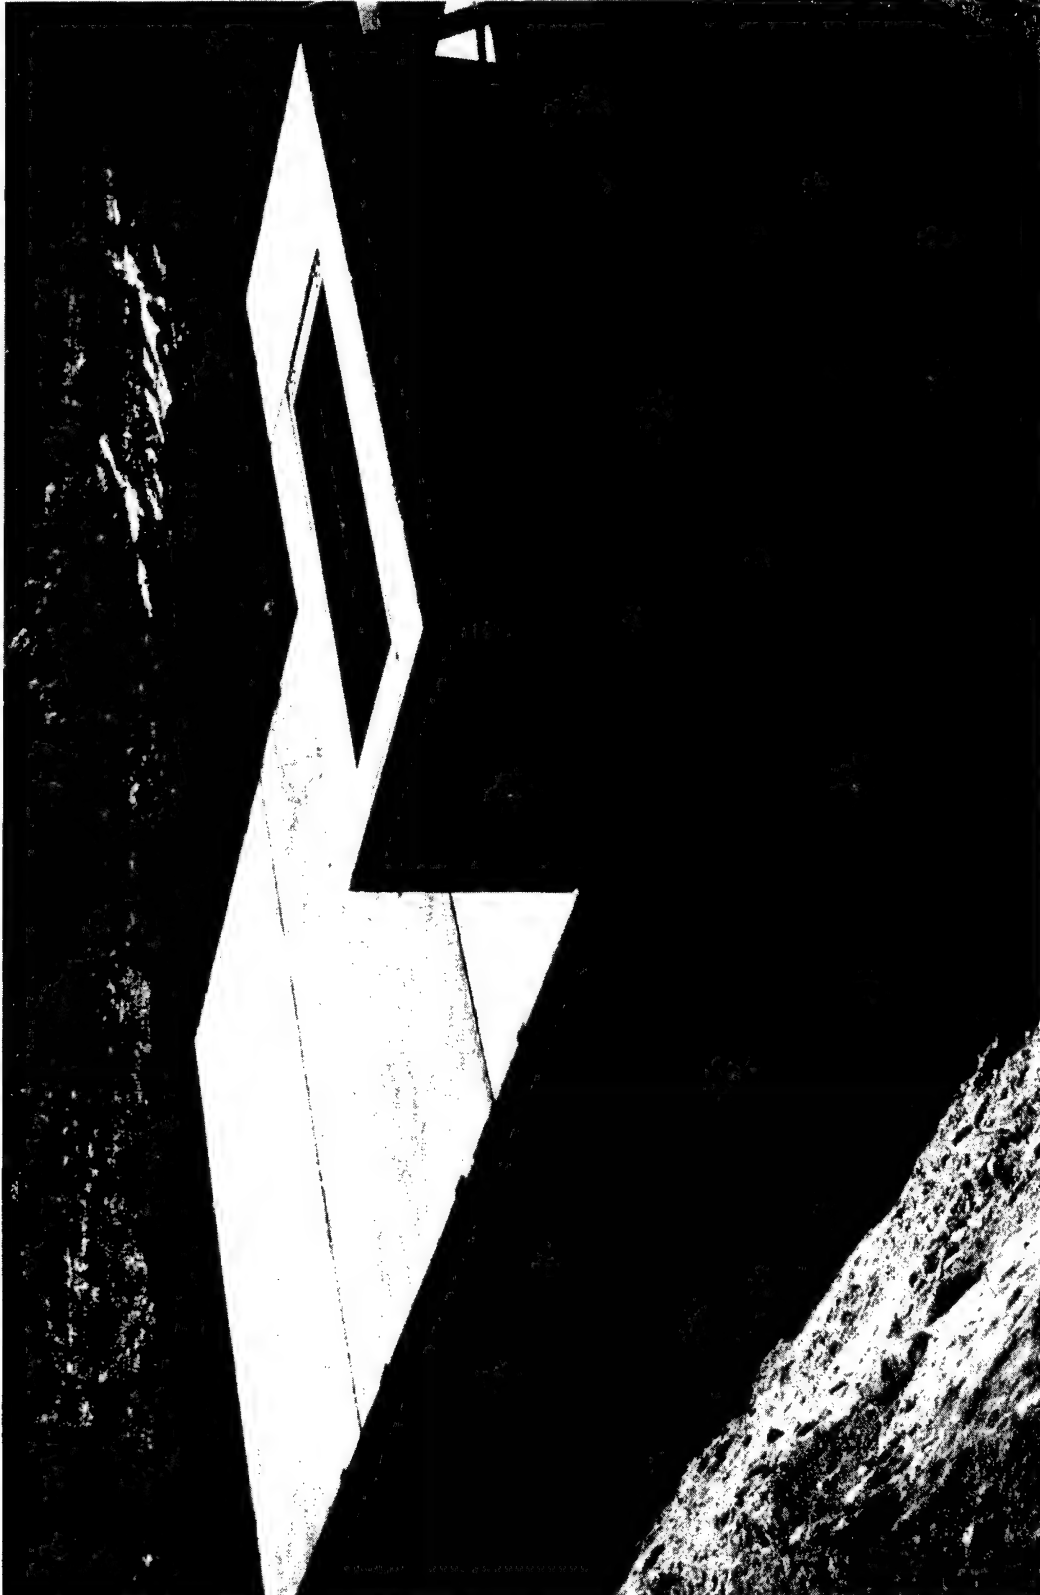


Figure 13. --Assembly of Manhole (page 10 of 10).

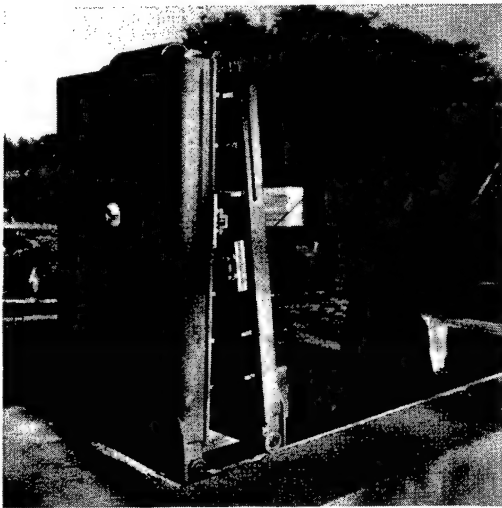
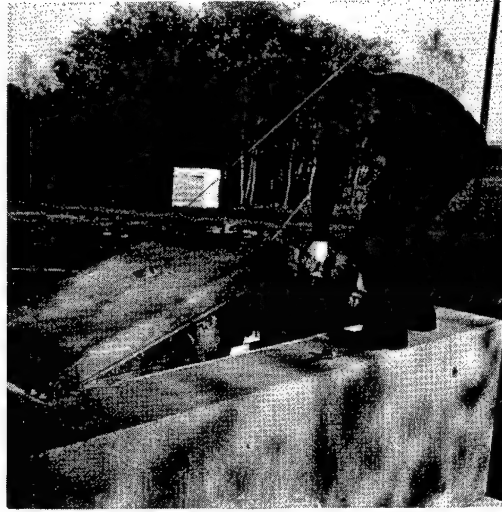
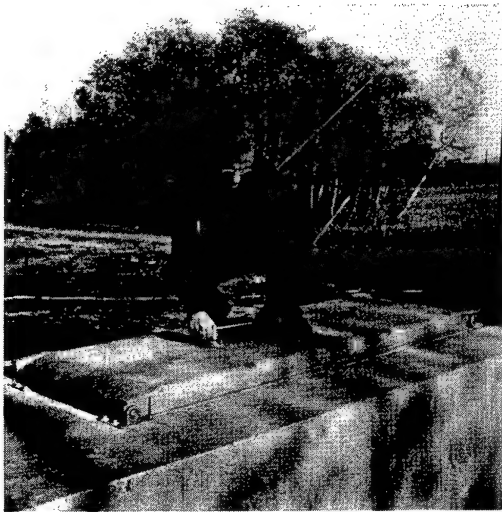


Figure 14. --Blast hatch used on SA Manhole.

The test installation is shown in plan in figure 15. As noted previously, the center of the manhole was located at the 60-psi range, with the long axis of the manhole oriented radially from GZ.

On the end of the manhole toward GZ, two 20-tube coaxial cables were installed to simulate a long cable run entering the manhole. Two types of cable entry pipes were installed: a 5-foot length of 4-inch ID PVC pipe (proposed for use), and an 8-foot length of 4-1/2-inch ID steel pipe. Each cable entry pipe penetrated the manhole wall and was grouted in place and bolted to the outer surface by means of a flanged connection. The cables were anchored externally to a deadman and were tied inside the manhole to the center structural steel frame to simulate the normal cable termination at a splice. The cables were installed at a depth of 4 feet below the original grade.

Two 40-foot lengths of conduit, one constructed of cement-asbestos, and the other of poly-vinyl-chloride (PVC), were located on the end of the manhole away from GZ. Both conduits had nominal inside diameters of 6 inches. The wall thickness of the relatively rigid cement-asbestos conduit was 0.70 inch, while that of the PVC conduit was 0.34 inch.

Shear protection for the transite conduit was provided by a nominal 12-inch diameter outer steel jacket, 6-feet long. The space between the jacket and conduit was filled with soft polyurethane foam. Shear protection for the PVC conduit consisted of a foam padding surrounding only the portion of conduit that projected through the wall.

The purpose of these tests was to evaluate the change due to blast in the alignment of conduit installed in a trench and at the interface with a manhole.

Bell Laboratories is currently engaged in the development of a waveguide transmission system for transcontinental communications. Unlike coaxial cables, low-loss performance of the waveguide requires a low level of geometric imperfection. Whereas failure in coaxial cables occurs only if the cable tears apart or an outer coaxial tube collapses, failure of the waveguide system could occur if the residual soil displacements are highly irregular, causing excessive curvature of the waveguide axis.

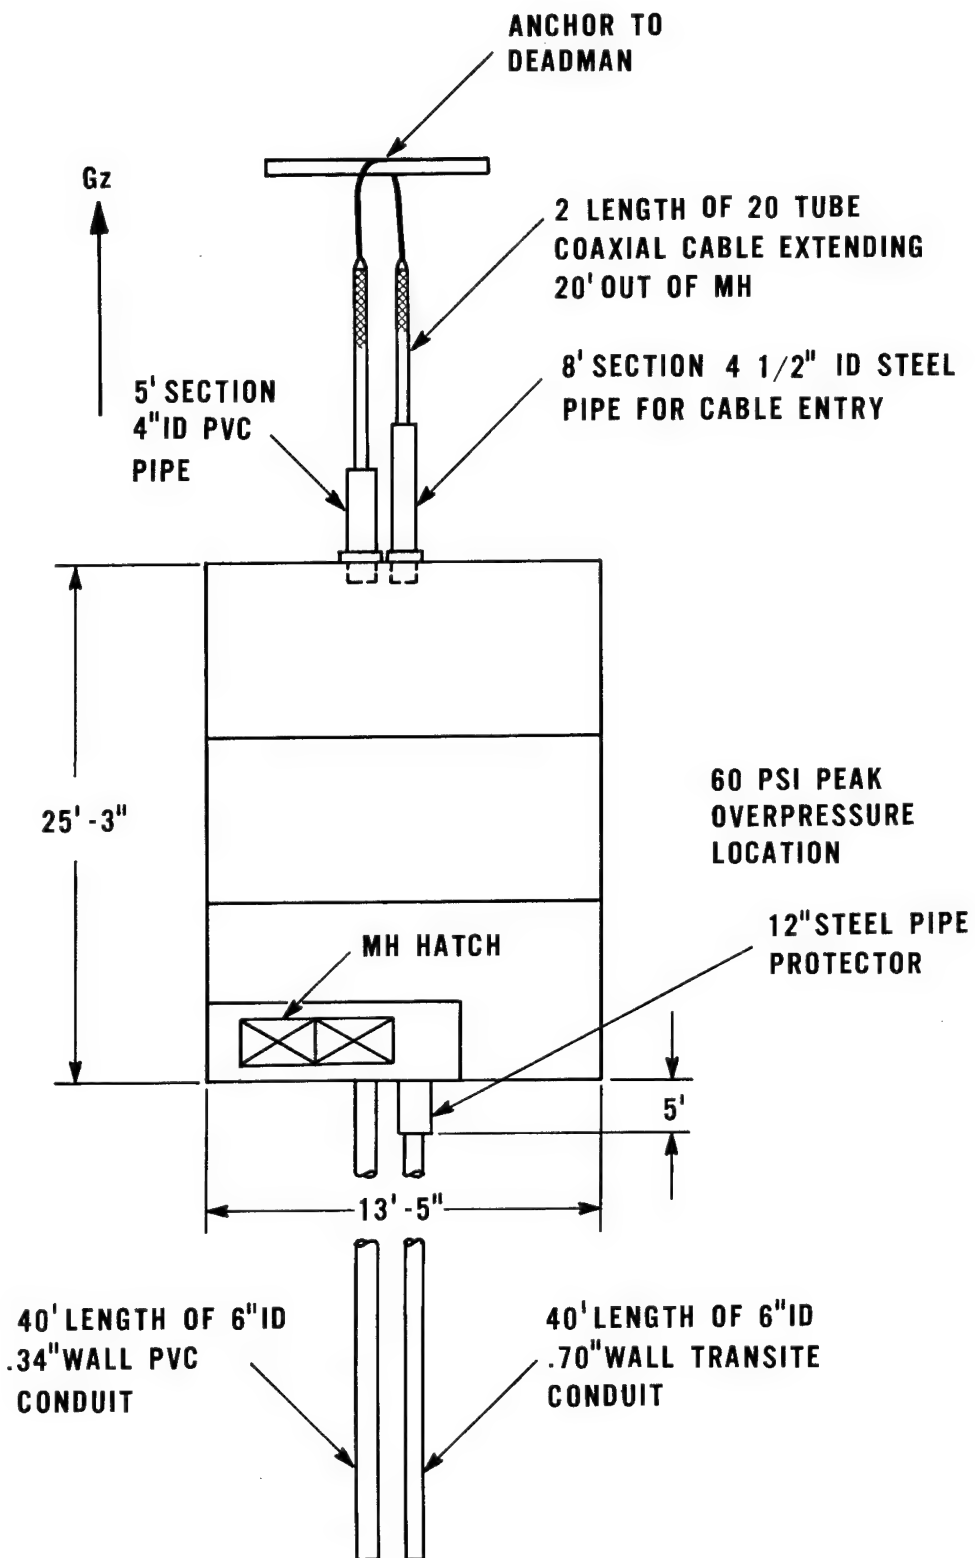


Figure 15. --Test installation.

Although the configuration of the buried installation has not yet been determined, it is likely that the waveguide will be housed in a conduit in a manner which isolates it from a certain amount of distortion of the conduit.

Some distortion will occur during initial installation, and this must be accounted for in the selection of repeater spacings. It is important to have an estimate of the distortions which may occur during the life of the installation or under blast loading, so that adequate compensation can be provided in the repeaters.

Figure 16 shows an elevation view of the conduit installation. The excavation region surrounding the building was somewhat larger than originally anticipated. In the area where the conduits and cable crossed the excavation region, the back-fill under the conduits and cables was compacted. The natural soil was pushed into the void against the manhole end-walls to a height just below the entry holes for the conduit and cable (about a 3-foot depth), after which about 1,000 gallons of water were used to partially compact the soil by "puddling." Then, a few inches of additional soil were added on top of the wet soil to permit additional compaction by means of an impact-type motor driver-compactor. The result of this process was less than an optimum soil compaction but modeled a situation likely to occur in actual practice.

To make measurements of the distortions of the conduit tubes before and after the blast, a small target was sighted through a telescope located inside the manhole. The target was pushed along the conduit bore from inside the manhole.

Figure 17 shows a view of the installation of the PVC conduit.

Two separate tests were performed adjacent to the large structure. A new design cast-aluminum manhole cover was installed on a cast-aluminum frame and fiberglass collar at the same overpressure range as the center of the precast concrete SA Manhole. Five 10-foot long sections of conduit of various stiffnesses were installed at a depth of 4 feet and at a range equal to that of the center of the 40-foot lengths of conduit. The objective of both of these experiments was to determine blast resistance and ability to survive the applied blast overpressure.

Included in this latter installation were three cement-asbestos conduits of 0.40-inch wall thickness, a PVC conduit with a 0.18-inch wall thickness, and a flexible, corrugated plastic conduit of nominal thickness 0.02 inch, corrugation

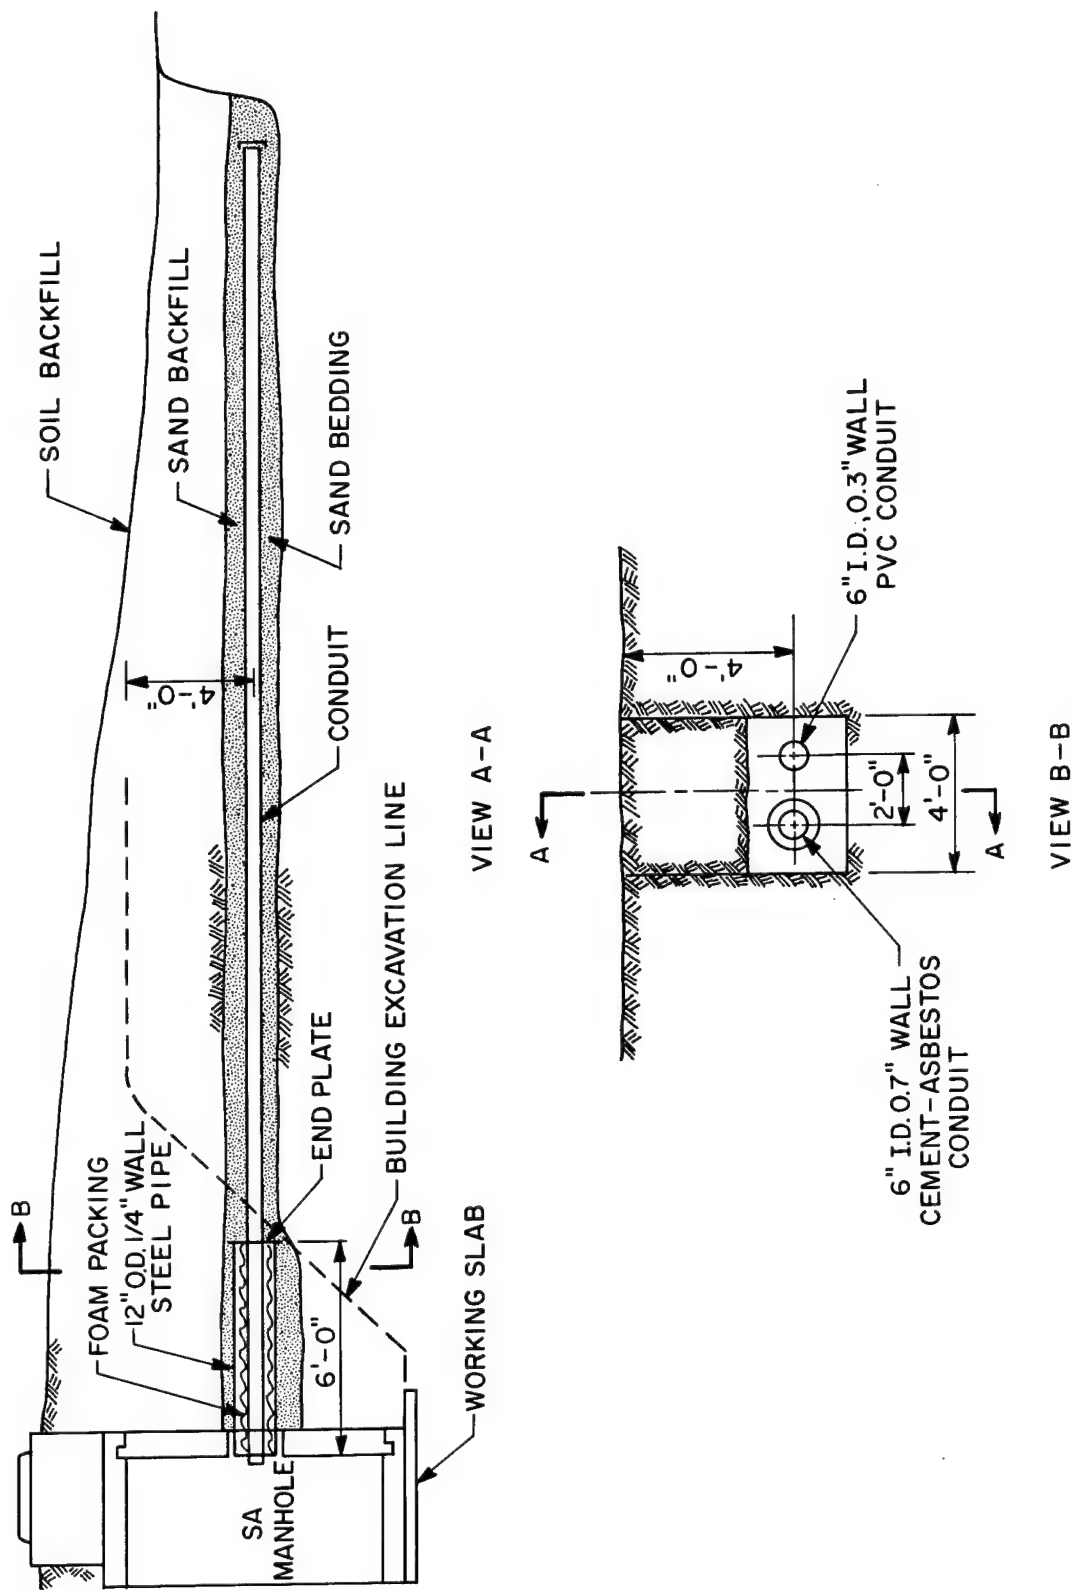


Figure 16. ---Elevation view of the conduit installation.



Figure 17. --Installation of the PVC conduit.

depth 0.2 inch, and corrugation pitch or "wavelength" of 0.25 inch. One of the cement-asbestos conduits had a nominal 5-inch inside diameter, but the rest were 6-inch conduits.

Although a great deal of care was exercised in the installation of the main conduit runs, the short, thin-walled conduits were installed using standard pipe-laying procedures. Sand was used as a bedding material in both cases, and sand backfill was placed over the conduit to a height of 12 inches for the main runs and 6 inches for the others. The bedding and backfill sand of the main runs was tamped with an impact type of soil compactor.

The location of all instrumentation for this project is shown in figure 18. The deflection gages in the structure were used primarily to determine relative movement between the side wall, end wall, roof, and base slabs. Gages D1 through D5 were of the cantilever beam type with two SR-4 strain gages cemented on the top and underside of the beam. One end of the beam was fixed securely on a slab, while contact to the adjacent slab was made by means of an adjustable screw with a pointed tip through the free end of the beam. The pointed tip engaged a blued steel plate which also provided a scratched record of deflections perpendicular to the movement of the cantilever beam. Gage D6, which measured displacement between the floor and roof of the structure, was of a slide-wire potentiometer type. Prior to the detonation, all deflection gages were calibrated and initial deflections applied to permit both positive and negative movements of the slabs to be recorded.

The following notation was employed for the deflection measurements:

- D1, D2 Horizontal deflection of side walls in two directions.
- D3 Vertical roof deflection relative to side wall.
- D4 Horizontal side wall deflection relative to roof.
- D5 Horizontal deflection of end wall relative to side wall.
- D6 Vertical displacement between roof and floor.

Accelerations A1 through A5 were measured at the locations and in the directions shown. Surface pressure gages P1 and P2 were placed along the expected 60-psi overpressure range and about 5 feet from each side wall of the structure.



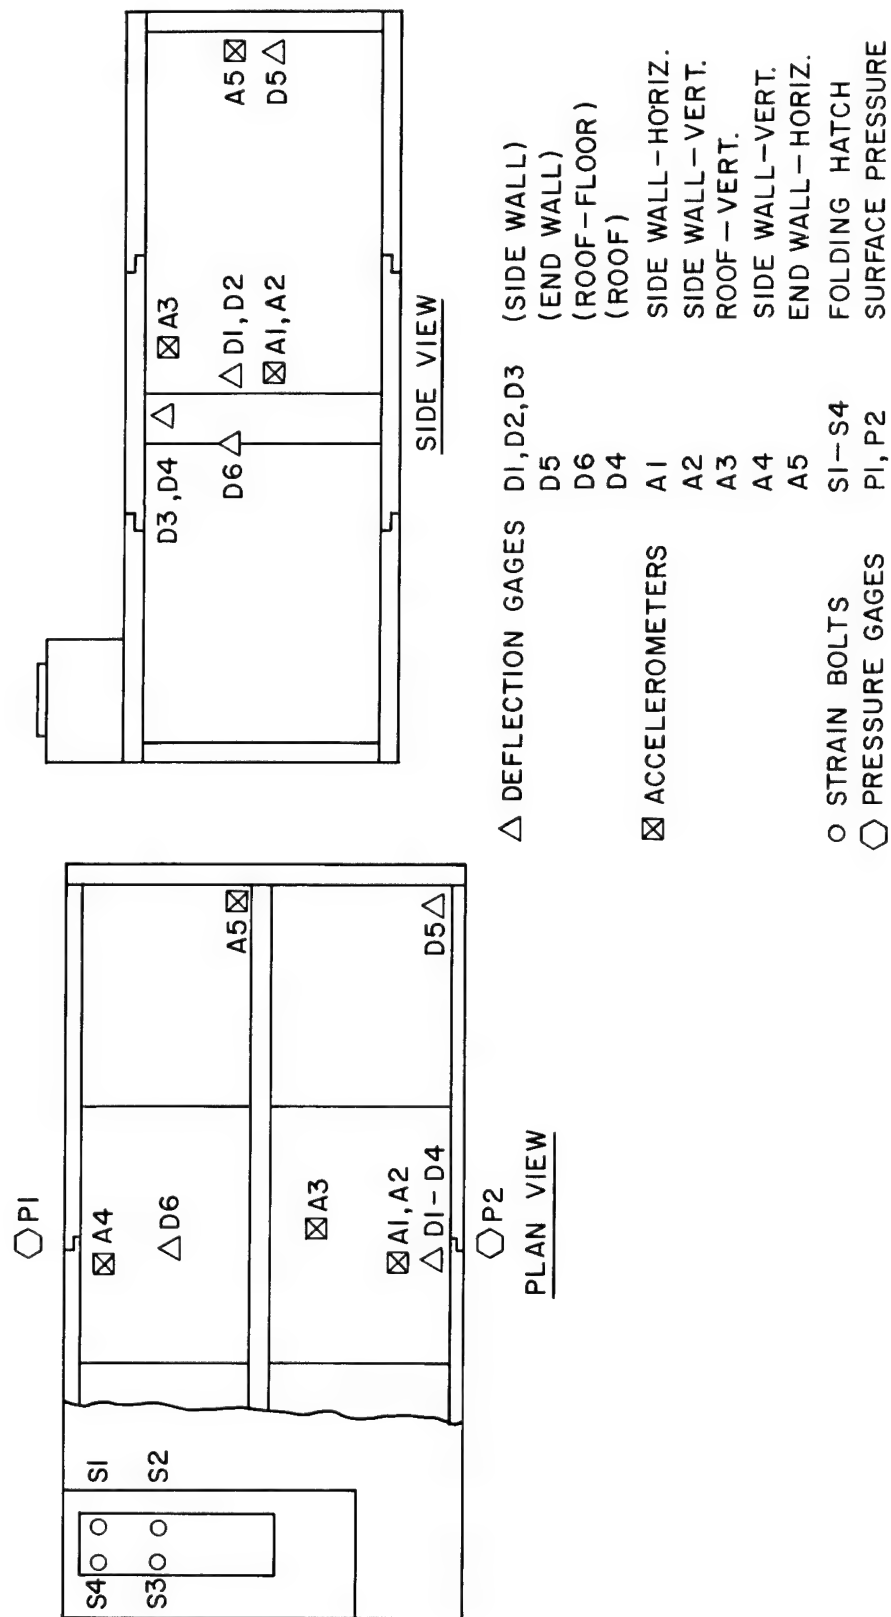


Figure 18. --Instrumentation.

Strain bolts S1 through S4, used to fasten the folding hatch in place, were secured with an initial load of approximately 1,000 pounds per bolt.

In addition to dynamic instrumentation, diagonal measurements were made inside the structure before and after the blast to determine if racking occurred. This was accomplished by using telescoping aluminum tubes with specially prepared ends. The tubes were graduated to facilitate measurement.

## RESULTS

Figure 19 shows a postshot view of the blast hatch. The hatch cover did not sustain damage and was still secured in place after the blast. The strain bolts, which had been preloaded to 1,000 pounds each, indicated very little rebound loading due to the blast. See table 1 for recorded measurements.

The structure developed some hairline cracks and some minor spalling. The damage was superficial, however, and would not be considered as having caused any weakening of the structure.

Surface pressure-gages P1 and P2 recorded pressures of 56 psi and 38 psi, respectively. These gages were checked after the blast and were found to be accurate. The recorded pressures were therefore considered to be actual pressures.

All deflection gages and accelerometers performed satisfactorily. The recorded tapes indicated the peak values noted in table 3.

Diagonal measurements of the structure interior indicated some slight changes which could be attributed to a compression of the butyl rubber gasket; however, racking of the structure did not occur. See table 2 for diagonal measurements before and after the shot.

In figure 20 the vertical axial deformations of the main conduits are shown. It was found that there were virtually no changes in the configurations of the two conduits over the full length in the horizontal plane (not shown) and over all but the first 10 feet in the vertical plane. Not only did substantial vertical deformation changes occur in the excavation region due to the blast, but initial alignment there was much more irregular. A circumferential crack was noted in the cement-asbestos conduit about 6-1/2 feet from the inside end. Beyond the 10-foot position, any changes that might have occurred were generally small and less than the estimated 0.10-inch possible error inherent in the measuring method. From 28 to 36 feet out, the measured deformations differed slightly from the initial readings for the cement-asbestos conduit, but the changes were upward, a movement which would not be expected. Thus, the data there were considered suspect on initial investigation.



Figure 19. --Postshot view of the blast hatch.

Table 1. --Recorded measurements of rebound forces

<u>Bolt Number</u>	<u>Load</u>	
S1	2,400 pounds	} Hatch cover rebound forces
S2	1,400 pounds	
S3	2,400 pounds	
S4	1,400 pounds	

Table 3. --Recorded peak values

<u>Gage</u>	<u>Expected Reading</u>	<u>Actual Reading</u>
D1	0.0625 inch	0.013 inch
D2	0.0625 inch	0.010 inch
D3	0.125 inch	0.087 inch
D4	0.125 inch	0.110 inch
D5	0.125 inch	0.125 inch
D6	0.250 inch	0.220 inch
A1	25 g's	±6 g's
A2	25 g's	±8 g's
A3	50 g's	+9 g's through 15 g's
A4	25 g's	±9 g's
A5	50 g's	±9 g's

Table 2. --Diagonal measurements of structure interior

Position	Initial Reading	Final Reading	
1	14 feet - 4-7/8 inches	14 feet - 4-3/4 inches	
2	14 feet - 4-7/8 inches	14 feet - 4-3/4 inches	
3	14 feet - 5-3/16 inches	14 feet - 4-15/16 inches	
4	14 feet - 5-1/16 inches	14 feet - 4-7/8 inches	(Diagonal measurements averaged 1/8 inch to 1/4 inch shortening.)
5	14 feet - 5-3/8 inches	14 feet - 5-1/8 inches	
6	14 feet - 5-3/16 inches	14 feet - 5 inches	
7	14 feet - 5-1/2 inches	14 feet - 5-1/2 inches	
8	14 feet - 5-1/4 inches	14 feet - 5-1/16 inches	

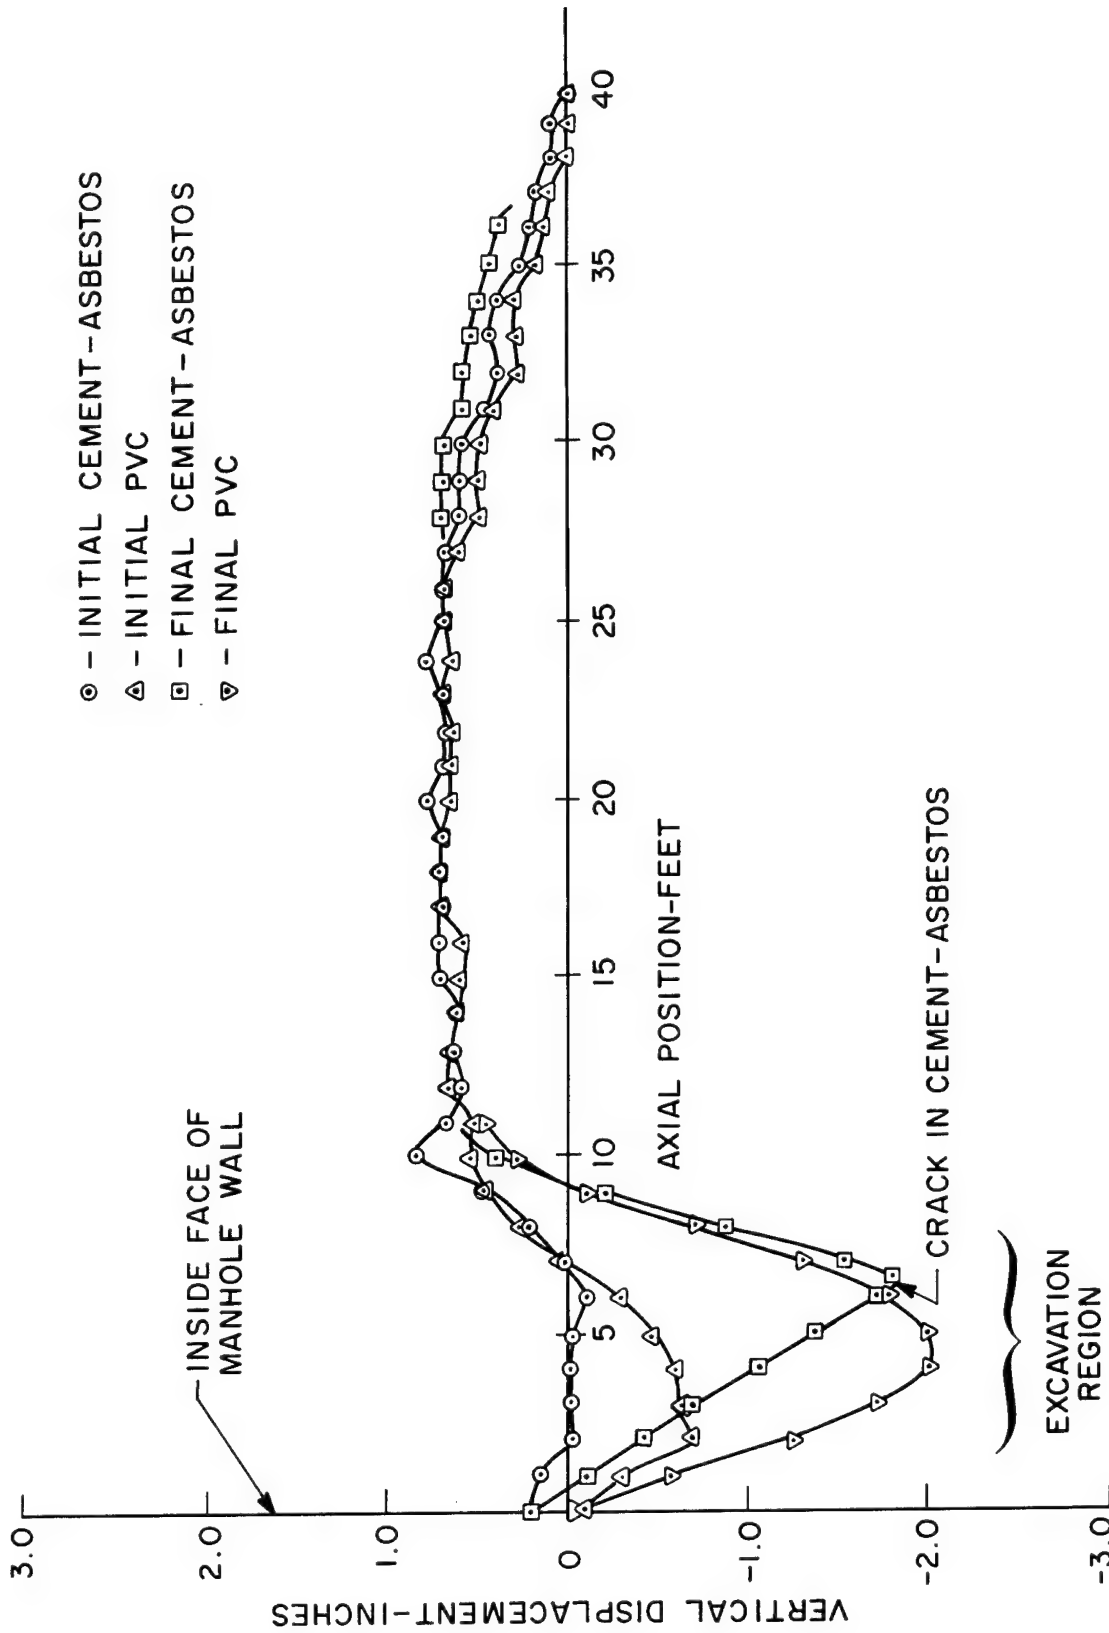


Figure 20. --Main conduit vertical axial deformations.



All of the thin-walled conduits survived, as was ascertained by inspection, looking into the ends of the conduits. It was not possible to determine whether there had been any appreciable ovaling except at the inspection ends. There was some ovaling at the end of the PVC conduit, with a major- to minor-diameter ratio of approximately 1.1. The other conduit ends appeared circular. A hair-line circumferential crack appeared in one of the 6-inch cement-asbestos conduits. This may have been due to an imperfect bedding and was not related to collapse phenomena.

The large coaxial cables survived the blast with no apparent damage. Both the PVC plastic and the steel pipes were bent downward on their outward ends by 3 to 5 inches; at the junction with the concrete wall, each had buckled slightly due to the high bending moment at that location.

## CONCLUSIONS

Three basic conclusions were drawn from the conduit experiment:

1. No appreciable vertical deformations occurred in the trenched conduit 4-1/2 feet below the surface at the nominal 50- to 40-psi region.
2. Commercial conduit in the 5- to 6-inch diameter range can survive this environment using standard installation procedures.
3. Some special treatment of the backfill in the excavation region under entrance pipes is required to limit conduit deformations.

Deflections and relative motions of adjacent wall slab or roof sections were small; they were on the order of 1/8-inch or less minimum to 1/4-inch maximum. Accelerations were somewhat lower than expected, ranging from 5 to 15 g's. Racking, or change in diagonal dimensions across the manhole, was minimal, with noted changes of 1/4 inch or less. It is apparent that this type of structure, with individual flat slabs interlocked together with only minimal ties and no moment carrying ability at joints, can survive the applied blast loading with very little relative motion between slabs.

Both cable entry protection designs survived the blast loading, but the deflections and buckling of the pipe indicate that such protection is needed and, if not provided, such loading would very likely damage the coaxial cables.

Although both the two-part folding blast hatch and the smaller one-piece cast-aluminum manhole cover survived the blast as installed, the low rebound forces recorded in the hold-down bolts of the blast hatch were unexpected. The rebound behavior of this blast hatch should be studied further.

## DIAL PACK DISTRIBUTION LIST

### COPIES

#### DEPARTMENT OF DEFENSE

- 12 DEFENSE DOCUMENTATION CENTER, CAMERON STATION,  
ALEXANDRIA, VIRGINIA 22314  
ATTN: TC
- 1 DIRECTOR, DEFENSE INTELLIGENCE AGENCY, WASHINGTON,  
D.C. 20301  
ATTN: DI-7B, PHYS. VUL. DIV., MR. FRANK DEEDS
- 22 DIRECTOR, DEFENSE NUCLEAR AGENCY, WASHINGTON, D.C.  
20305  
ATTN: DDST  
ATTN: APSI (ARCHIVES)  
ATTN: SPLN, MR. JACK R. KELSO  
ATTN: APTL, TECHNICAL LIBRARY (2 CYS)  
ATTN: MAJOR WILLIAM J. SHEPARD (15 CYS)  
ATTN: SPAS  
ATTN: SPSS
- 1 DEPARTMENT OF DEFENSE EXPLOSIVES SAFETY BOARD,  
RM-GB270, FORRESTAL BUILDING, WASHINGTON, D.C. 20301  
ATTN: MR. RUSSEL G. PERKINS
- 2 COMMANDER, FIELD COMMAND, DEFENSE NUCLEAR AGENCY,  
KIRTLAND AFB, NEW MEXICO 87115  
ATTN: TECHNICAL LIBRARY, FCTA-A  
ATTN: FCTD-T
- 1 CHIEF, LIVERMORE DIVISION, FIELD COMMAND, DNA,  
LAWRENCE LIVERMORE LABORATORY, P.O. BOX 808,  
LIVERMORE, CALIFORNIA 94550  
ATTN: FCTA-D
- 1 DIRECTOR, WEAPONS SYSTEMS EVALUATION GROUP, ODDR&E,  
OFFICE, SECRETARY OF DEFENSE, 400 ARMY-NAVY DRIVE,  
WASHINGTON, D.C. 20305  
ATTN: CAPT DONALD E. MCCOY, USN

#### DEPARTMENT OF THE ARMY

- 1 COMMANDING OFFICER, ABERDEEN PROVING GROUND,  
ABERDEEN PROVING GROUND, MARYLAND 21005  
ATTN: TECHNICAL LIBRARY

COPIES

DEPARTMENT OF THE ARMY (CONTINUED)

- 8     COMMANDING OFFICER, ABERDEEN RESEARCH AND  
DEVELOPMENT CENTER, ABERDEEN PROVING GROUND,  
MARYLAND 21005  
ATTN: MR. R. N. SCHUMACHER  
ATTN: MR. R. E. REISLER  
ATTN: MR. R. P. LONG  
ATTN: MR. J. H. KEEFER  
ATTN: MR. L. GIGLIO-TOS  
ATTN: MR. N. H. ETHRIDGE  
ATTN: AMXBR-TB, MR. JULIUS J. MESZAROS  
ATTN: DR. N. J. HUFFINGTON
- 1     DIRECTOR, ADVANCED BALLISTIC MISSILE DEFENSE AGENCY,  
COMMONWEALTH BUILDING, 1320 WILSON BOULEVARD,  
ARLINGTON, VIRGINIA 22209  
ATTN: DR. JACOB B. GILSTEIN
- 1     COMMANDING OFFICER, ARMY COLD REGION RESEARCH  
ENGINEERING LAB, P.O. BOX 282, HANOVER, NEW HAMPSHIRE  
03755
- 1     COMMANDING OFFICER, ARMY ENGINEER EXPLOSIVE  
EXCAVATION RESEARCH OFFICE, LAWRENCE LIVERMORE  
LABORATORY, LIVERMORE, CALIFORNIA 94550
- 8     DIRECTOR, ARMY ENGINEER WATERWAYS EXPERIMENT STATION,  
BOX 631, VICKSBURG, MISSISSIPPI 39180  
ATTN: WESNV  
ATTN: MR. G. E. ALBRITTON  
ATTN: MR. G. L. ARBUTHNOT  
ATTN: MR. T. E. KENNEDY  
ATTN: MR. J. GATZ  
ATTN: MR. D. W. MURRELL  
ATTN: MR. A. D. ROOKE  
ATTN: MR. J. N. STRANGE
- 1     CHIEF, ARMY SATELLITE COMMUNICATIONS AGENCY, FORT  
MONMOUTH, NEW JERSEY 07703  
ATTN: LTC MCGIVERN
- 1     COMMANDING OFFICER, ARMY TERRESTRIAL SCIENCES CENTER,  
P.O. BOX 282, HANOVER, NEW HAMPSHIRE 03755

COPIES

DEPARTMENT OF THE ARMY (CONTINUED)

- 1 ASSISTANT CHIEF OF STAFF FOR FORCE DEVELOPMENT,  
DEPARTMENT OF THE ARMY, WASHINGTON, D.C. 20310  
ATTN: DIRECTOR OF CHEMICAL AND NUCLEAR OPERATIONS
- 2 CHIEF OF ENGINEERS, DEPARTMENT OF THE ARMY,  
WASHINGTON, D.C. 20314  
ATTN: ENGME-RD  
ATTN: LTC G. CHASE
- 1 DEFENSE CIVIL PREPAREDNESS AGENCY, WASHINGTON, D.C.  
20301  
ATTN: STAFF DIRECTOR, RE(SR), MR. GEORGE N. SISSON
- 1 COMMANDING OFFICER, FRANKFORD ARSENAL, BRIDGE AND  
TACONY STREETS, PHILADELPHIA, PENNSYLVANIA 19137  
ATTN: MR. B. SCHEIN
- 1 DEPARTMENT OF THE ARMY, HARRY DIAMOND LABORATORIES,  
WASHINGTON, D.C. 20438  
ATTN: AMXDO-NP, MR. F. M. WIMINITZ
- 1 COMMANDING OFFICER, PICATINNY ARSENAL, DOVER, NEW  
JERSEY 07801  
ATTN: MR. A. FLUGER
- 1 SAFEGUARD SYSTEM MANAGER, SAFEGUARD SYSTEM OFFICE,  
1300 WILSON BOULEVARD, ARLINGTON, VIRGINIA 22209  
ATTN: CSSSO
- 2 DIRECTOR, U.S. ARMY ADVANCED BALLISTIC MISSILE DEFENSE  
AGENCY, HUNTSVILLE OFFICE, P.O. BOX 1500, HUNTSVILLE,  
ALABAMA 35807  
ATTN: CRDABH-S, MR. MELVIN T. CAPPS
- 1 U.S. ARMY COMBAT DEVELOPMENTS COMMAND, NUCLEAR  
AGENCY, FORT BLISS, TEXAS 79916
- 1 CHIEF, U.S. ARMY COMBAT DEVELOPMENTS COMMAND,  
COMMUNICATIONS-ELECTRONICS AGENCY, FORT MONMOUTH,  
NEW JERSEY 07703  
ATTN: CSG-CE-M
- 1 COMMANDING GENERAL, U.S. ARMY COMPUTER SYSTEMS  
COMMAND, FORT BELVOIR, VIRGINIA 22060  
ATTN: CSC-EN

COPIES

DEPARTMENT OF THE ARMY (CONTINUED)

- 2 COMMANDING GENERAL, U.S. ARMY ELECTRONICS COMMAND,  
FORT MONMOUTH, NEW JERSEY 07703  
ATTN: AMSEL-GG-EI  
ATTN: AMSEL-KL-I
- 3 COMMANDING GENERAL, U.S. ARMY MATERIEL COMMAND,  
WASHINGTON, D.C. 20315  
ATTN: AMCRD-B  
ATTN: AMCRD-BN-RE-2, MR. JOHN J. F. CORRIGAN  
ATTN: MR. B. H. STOUT
- 1 COMMANDING GENERAL, U.S. ARMY MISSILE COMMAND,  
REDSTONE ARSENAL, HUNTSVILLE, ALABAMA 35809  
ATTN: AMSMI-PLD, MR. BOUNDS
- 1 COMMANDING OFFICER, U.S. ARMY MOBILITY EQUIPMENT R  
AND D CENTER, FORT BELVOIR, VIRGINIA 22060  
ATTN: SMEFB-EAX, MR. D. B. DINGER
- 1 COMMANDING GENERAL, U.S. ARMY SAFEGUARD SYSTEM  
COMMAND, P.O. BOX 1500, HUNTSVILLE, ALABAMA 35807  
ATTN: SSC-DH, COL ROBERT A. PURPLE
- 1 COMMANDING GENERAL, U.S. ARMY TANK AUTOMOTIVE  
COMMAND, WARREN, MICHIGAN 48089  
ATTN: MR. C. HENNE
- 1 COMMANDING GENERAL, U.S. ARMY TEST AND EVALUATION  
COMMAND, ABERDEEN PROVING GROUND, MARYLAND 21005  
ATTN: AMSTE-NB
- 1 DEPARTMENT OF THE ARMY, U.S. ARMY WEAPONS COMMAND  
HEADQUARTERS, ROCK ISLAND, ILLINOIS 61201  
ATTN: MR. R. O. BORDER
- 1 COMMANDING GENERAL, WHITE SANDS MISSILE RANGE, NEW  
MEXICO 88002  
ATTN: TE-N, MR. MARVIN P. SQUIRES

DEPARTMENT OF THE NAVY

- 1 CHIEF OF NAVAL MATERIAL, NAVY DEPARTMENT, WASHINGTON,  
D.C. 20360  
ATTN: MAT 0323, MR. IRVING JAFFE

COPIES

DEPARTMENT OF THE NAVY (CONTINUED)

- 1 CHIEF OF NAVAL OPERATIONS, NAVY DEPARTMENT,  
WASHINGTON, D.C. 20350  
ATTN: OP-985F, CDR STOCKING
- 2 CHIEF OF NAVAL RESEARCH, DEPARTMENT OF THE NAVY,  
ARLINGTON, VIRGINIA 22217  
ATTN: CODE 418, DR. THOMAS P. QUINN  
ATTN: TECHNICAL INFORMATION SERVICES
- 7 COMMANDING OFFICER, NAVAL CIVIL ENGINEERING  
LABORATORY, PORT HUENEME, CALIFORNIA 93043  
ATTN: DR. WARREN A. SHAW  
ATTN: MR. J. R. ALLGOOD  
ATTN: MR. R. S. CHAPLER  
ATTN: MR. J. A. NORBUTAS  
ATTN: MR. R. H. SEABOLD  
ATTN: MR. S. K. TAKAHASHI  
ATTN: MR. D. E. WILLIAMS
- 1 COMMANDER, NAVAL ELECTRONIC SYSTEMS COMMAND  
HEADQUARTERS, WASHINGTON, D.C. 20360  
ATTN: PME 117-21
- 1 COMMANDER, NAVAL FACILITIES ENGINEERING COMMAND,  
COMMAND HEADQUARTERS, WASHINGTON, D.C. 20390  
ATTN: CODE 03A, MR. STANLEY ROCKEFELLER
- 2 COMMANDER, NAVAL ORDNANCE LABORATORY, SILVER SPRING,  
MARYLAND 20910  
ATTN: CODE 121, NAVY NUCLEAR PROGRAMS OFFICE  
ATTN: CODE 241, MR. JOSEPH PETES
- 1 COMMANDER, NAVAL ORDNANCE SYSTEMS COMMAND  
HEADQUARTERS, WASHINGTON, D.C. 20360  
ATTN: ORD-035D, MR. WILLIAM W. BLAINE
- 1 DIRECTOR, NAVAL RESEARCH LABORATORY, WASHINGTON, D.C.  
20390
- 2 COMMANDER, NAVAL SHIP RESEARCH AND DEVELOPMENT  
CENTER, BETHESDA, MARYLAND 20034  
ATTN: CODE 745, MR. EDWARD T. HABIB  
ATTN: MR. W. R. CONLEY

COPIES

DEPARTMENT OF THE NAVY (CONTINUED)

- 1 COMMANDER, NAVAL SHIP SYSTEMS COMMAND, NAVAL SHIP  
SYSTEMS COMMAND HEADQUARTERS, WASHINGTON, D.C. 20360  
ATTN: SHIPS 03541, MR. WILLIAM S. BROWN
- 1 COMMANDER, NAVAL WEAPONS CENTER, CHINA LAKE,  
CALIFORNIA 93555
- 1 COMMANDER, NAVAL WEAPONS LABORATORY, DAHLGREN,  
VIRGINIA 22448  
ATTN: TIEC

DEPARTMENT OF THE AIR FORCE

- 1 COMMANDER, AF SPECIAL WEAPONS CENTER, AFSC, KIRTLAND  
AFB, NEW MEXICO 87117  
ATTN: MR. R. CLARK
- 6 AF WEAPONS LABORATORY, AFSC, KIRTLAND AFB, NEW MEXICO  
87117  
ATTN: MR. J. L. BRATTON  
ATTN: MAJOR WILLIAM WHITTAKER  
ATTN: DEV, DR. HENRY COOPER  
ATTN: MR. C. E. NEEDHAM  
ATTN: DOGL, TECHNICAL LIBRARY  
ATTN: MAJOR LEIGH
- 2 CHIEF, AIR FORCE AUDIO-VISUAL CENTER, NORTON AFB,  
CALIFORNIA 92409  
ATTN: MR. K. HACKMAN  
ATTN: MR. G. PRATT
- 1 HEADQUARTERS, AIR FORCE SYSTEMS COMMAND, ANDREWS  
AFB, WASHINGTON, D.C. 20331  
ATTN: DEE
- 2 CHIEF OF STAFF, U.S. AIR FORCE, WASHINGTON, D.C. 20330  
ATTN: RD (DCS, RESEARCH & DEVELOPMENT)
- 1 SPACE AND MISSILE SYSTEMS ORGANIZATION, AFSC, NORTON  
AFB, CALIFORNIA 92409  
ATTN: LIEUTENANT COLONEL J. CAHOON



COPIES

ATOMIC ENERGY COMMISSION

- 1 ASSISTANT GENERAL MANAGER FOR MILITARY APPLICATION,  
U.S. ATOMIC ENERGY COMMISSION, WASHINGTON, D. C. 20545  
ATTN: DOCUMENT CONTROL FOR RES. & DEV. BRANCH
- 1 SANDIA LABORATORIES, P.O. BOX 5800, ALBUQUERQUE, NEW  
MEXICO 87115  
ATTN: DOCUMENT CONTROL FOR MR. J. W. REED

OTHER GOVERNMENT AGENCY

- 1 DEPARTMENT OF THE INTERIOR, U.S. GEOLOGICAL SURVEY,  
601 EAST CEDAR STREET, FLAGSTAFF, ARIZONA 86001  
ATTN: DR. DAVID J. RODDY, ASTROGEOLOGIC STUDIES

DEPARTMENT OF DEFENSE CONTRACTORS

- 3 BELL TELEPHONE LABORATORIES, INC., MOUNTAIN AVENUE,  
MURRAY HILL, NEW JERSEY 07971  
ATTN: DR. E. F. WITT  
ATTN: MR. MEAD F. STEVENS  
ATTN: MR. R. W. MAYO
- 1 GENERAL AMERICAN TRANSPORTATION CORPORATION, GENERAL  
AMERICAN RESEARCH DIVISION, 7449 NORTH NATCHEZ AVENUE,  
NILES, ILLINOIS 60648
- 1 GENERAL ELECTRIC COMPANY, TEMPO-CENTER FOR ADVANCED  
STUDIES, 816 STATE STREET (P.O. DRAWER QQ), SANTA  
BARBARA, CALIFORNIA 93102  
ATTN: DASAC
- 3 LOVELACE FOUNDATION FOR MEDICAL EDUCATION AND RES.,  
5200 GIBSON BOULEVARD, SE., ALBUQUERQUE, NEW MEXICO  
87108  
ATTN: PRESIDENT-DIRECTOR, DR. CLAYTON S. WHITE  
ATTN: ASSOCIATE SCIENTIST, DR. E. ROYCE FLETCHER  
ATTN: DR. D. R. RICHMOND
- 1 UNIVERSITY OF NEW MEXICO, DEPT. OF CAMPUS SECURITY AND  
POLICE, ALBUQUERQUE, NEW MEXICO 87106  
ATTN: ERIC H. WANG CIVIL ENG. RESEARCH FACILITY
- 2 PHYSICS INTERNATIONAL COMPANY, 2700 MERCED STREET,  
SAN LEANDRO, CALIFORNIA 94577  
ATTN: MR. C. T. VINCENT  
ATTN: MR. FRED M. SAUER

COPIES

DEPARTMENT OF DEFENSE CONTRACTORS (CONTINUED)

- 1 TRW SYSTEMS GROUP, ONE SPACE PARK, REDONDO BEACH,  
CALIFORNIA 90278  
ATTN: MR. F. A. FEIPER
- 1 URS RESEARCH COMPANY, 155 BOVET ROAD, SAN MATEO,  
CALIFORNIA 94402  
ATTN: MR. C. WILTON
- 1 WEIDLINGER, PAUL, CONSULTING ENGINEER, 110 EAST 59TH  
STREET, NEW YORK, NEW YORK 10022  
ATTN: DR. MELVIN L. BARON

MISCELLANEOUS

- 1 CANADIAN GENERAL ELECTRIC, 3603 8TH STREET, SE.,  
CALGARY, ALBERTA, CANADA  
ATTN: MR. D. J. DALTON
- 7 CHIEF SUPERINTENDENT, DEFENCE RESEARCH ESTABLISHMENT,  
SUFFIELD, RALSTON, ALBERTA, CANADA  
ATTN: MR. A. P. R. LAMBERT  
ATTN: MR. A. M. PATTERSON  
ATTN: MR. R. C. WYLD  
ATTN: MR. F. DAVEY  
ATTN: MR. R. B. HARVEY  
ATTN: MR. D. LITTLE  
ATTN: MR. W. HART

UNCLASSIFIED

Security Classification

DOCUMENT CONTROL DATA - R & D		
(Security classification of title, body of abstract and indexing annotation must be entered when the overall report is classified)		
1. ORIGINATING ACTIVITY (Corporate author) Defense Nuclear Agency Washington, D. C. 20305		2a. REPORT SECURITY CLASSIFICATION UNCLASSIFIED
		2b. GROUP
3. REPORT TITLE Test of Precast Concrete Underground Structure (U)		
4. DESCRIPTIVE NOTES (Type of report and inclusive dates) Final Report of Project LN-318, DIAL PACK Event, accomplished on MIDDLE NORTH Series.		
5. AUTHOR(S) (First name, middle initial, last name) R. W. Mayo, Bell Laboratories, Whippany Road, Whippany, New Jersey 07981		
6. REPORT DATE 24 November 1972	7a. TOTAL NO. OF PAGES 50	7b. NO. OF REFS None
8a. CONTRACT OR GRANT NO.	9a. ORIGINATOR'S REPORT NUMBER(S) POR-6741 (WT-6741)	
b. PROJECT NO. LN-318		
c.	9b. OTHER REPORT NO(S) (Any other numbers that may be assigned this report)	
d.		
10. DISTRIBUTION STATEMENT Approved for public release; distribution unlimited.		
11. SUPPLEMENTARY NOTES	12. SPONSORING MILITARY ACTIVITY DOD/DNA	
13. ABSTRACT DIAL PACK Event of the MIDDLE NORTH Series, Bell Laboratories Project LN-318, involved the evaluation of the blast-induced response of the SA Manhole. The SA Manhole was a full-size, segmented, precast-concrete hardened structure, to be used by the Long Lines Department of American Telephone and Telegraph Company, to house electronic repeater equipment. Testing was designed to determine the extent of cracking, equipment environments, and overall structural response.		

DD FORM 1473

REPLACES DD FORM 1473, 1 JAN 64, WHICH IS OBSOLETE FOR ARMY USE.

UNCLASSIFIED

Security Classification

UNCLASSIFIED

Security Classification

14. KEY WORDS	LINK A		LINK B		LINK C	
	ROLE	WT	ROLE	WT	ROLE	WT
MIDDLE NORTH Series						
DIAL PACK Event						
Hardened manholes						
SA Manhole						
Precast-concrete hardened manhole						
Blast damage						

UNCLASSIFIED

Security Classification
